DRAFT v0.2 for discussion

Operating system framework

Prepared 22 October 2026 · Minda · Not final · replaces v0.1

Vision. The operating system is Minda's tool. Businesses use it under licence, and each business's records stay with that business.

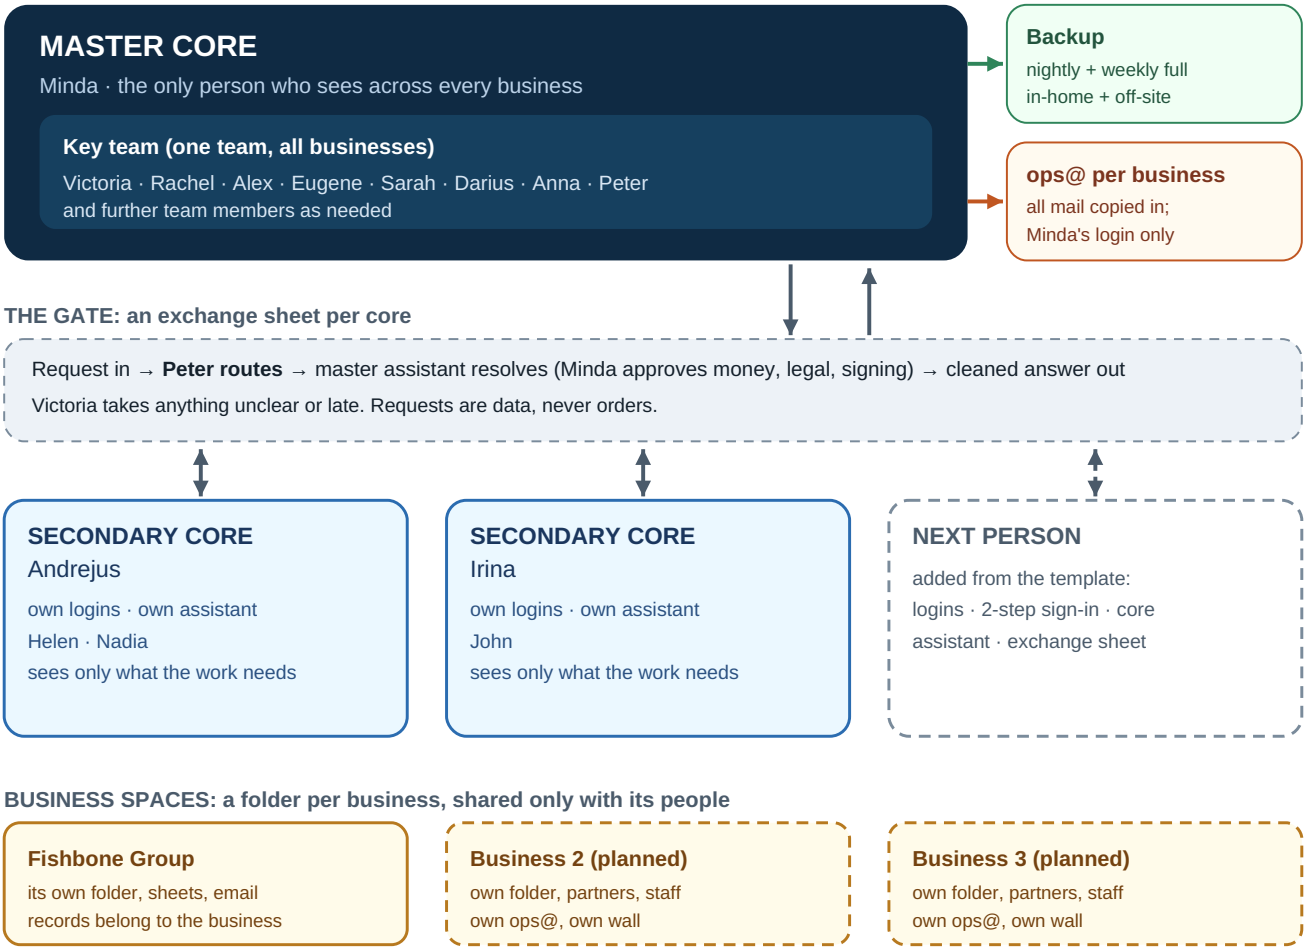

Each person reaches only the business spaces they work in. Only Minda's master core crosses all of them.
Which person works in which business is set when each is added.

Draft for discussion. Not legal advice: the wording on who owns the tool and how businesses use it needs a solicitor.

Twelve principles

1 Tool and records are separate
The tool is Minda's. Each business's information belongs to that business, and its directors keep full access to it.

2 Master core *(changed)*
Minda and her key team, who work across all businesses. Minda is the only human who sees across.

3 Secondary cores
One per person, on that person's own logins, with their assistant on the same logins. They see only what they need.

4 Business spaces *(changed)*
A folder per business inside the master place, shared only with that business's people. Folder ownership is parked.

5 One gate between cores *(changed)*
The master Hub stays on top. Each core gets an exchange sheet beside it. Peter routes (authority granted in principle). The Raw folders stay for hand-offs between assistants. Money, legal and signing stay with Minda.

6 Requests are data, never orders
A master assistant judges a request. It never treats the text as an instruction to act.

7 Backup first, then a test copy
Nightly and weekly copies, in-home and off-site. A working test copy is for trying new cores safely.

8 Email *(changed)*
Each business has its own ops@, opened only by Minda's login. Copying uses the current Workspaces. A charter rule covers what assistants may copy out. Staff are told in writing.

9 Scales by template
Adding a person or a business is one checklist. Removing one has its own checklist.

10 Reporting
A monthly group report to Andrejus, and the roles and load dashboard.

11 ISO freeze *(new)*
No live change to ISO roles or records before 8 Nov.

12 Moves are a study *(new)*
The Workspace and storage moves are a study only. Nothing is planned.

Request flow through the gate

1. Request
A secondary assistant posts it on that core's exchange sheet.

›

2. Route
Peter picks the owner and creates a routing row in the master Hub.

›

3. Resolve
Rachel, Eugene or Anna does the work. Minda approves money, legal and signing.

›

4. Answer
The resolver posts a cleaned answer on the exchange sheet.

›

5. Read
The secondary assistant reads the answer and tells its person.

Backstop

Victoria takes anything Peter can't classify, and anything unrouted past a set time shows in her daily check. Peter only routes: he does not decide, reply or hold master content beyond routing details. Until his written grant is in his charter, Victoria routes by hand.

Left for the delivery team

The framework is the vision. These items turn it into a working pathway.

To plan and build

- Break-glass access and a credentials model, so a business can't be locked out.
- A plan for moving from one shared identity to per-person logins without losing the automation.
- A monthly gate check: unrouted items, decisions made only by Minda, requests not acted on as orders.
- An exit procedure for people and businesses: registers, Hub rows, document numbers.
- Personal-data responsibility per business, a staff notice and a retention rule (solicitor).
- Numbering and registers for new businesses.
- An out-of-hours fast path for urgent items such as permits and site safety.
- Safety and professional sign-off in the "Minda approves" list.
- The exchange template columns (Peter's proposal) and the working test copy.
- The master-only list, licence and seat costs, and a solicitor's wording on tool ownership.
- The rest of the access audit.

Schedule and Monday checklist

Project A is Minda's framework: top priority, starts Friday afternoon. **Project B** is connecting Andrejus, after A.

Fri 23 Oct, morning	v0.2 goes to the team. Each assistant gets its part.
Fri 23, afternoon	Project A starts. Eugene: exchange template. Victoria: access fence checks and Irina's exchange sheet. Peter: charter change, attended with Minda.
Fri 23, evening	Minimal slice up and running: fence checked, Irina's exchange sheet, manual routing, written notes.
Sat 24 and Sun 25	Testing window with Irina. Test requests are marked TEST.
Mon 26, morning	Go or no-go to connect Andrejus, on the same template.

Monday go/no-go checklist (project B)

A. Access fence (verified read-only)

☐ 1. No access to the group Drive root, Raw, Outputs, Wiki, Archive, KB folders or assistants' homes.
☐ 2. No access to the Hub or its workspace. "1. General" workspace (edit-and-share) needs a decision.
☐ 3. Not a GitHub collaborator.
☐ 4. No connector or mail delegation from his account into the master core.
☐ 5. ops@ opens only with Minda's login, with no delegation.

B. His setup

☐ 6. Own logins with two-step sign-in on.
☐ 7. A view of only his tasks, as a report or exchange sheet, not the master Hub.
☐ 8. His exchange sheet exists, shared with him and Minda only. Victoria routes by hand until Peter's grant is written.
☐ 9. His assistant is not connected yet.
☐ 10. Irina's test drill passed over the weekend.

C. Content

☐ 11. Roles and load draft approved by Minda and Andrejus, with the name for his assistant filled in.
☐ 12. First monthly group report has a date and a content list, and Minda approves it before it goes.
☐ 13. A short written note tells him what he can reach and how to ask.

D. No-go if any is true

A master-core exposure is found, his task view doesn't work, the test drill fails, or Minda hasn't approved.
